


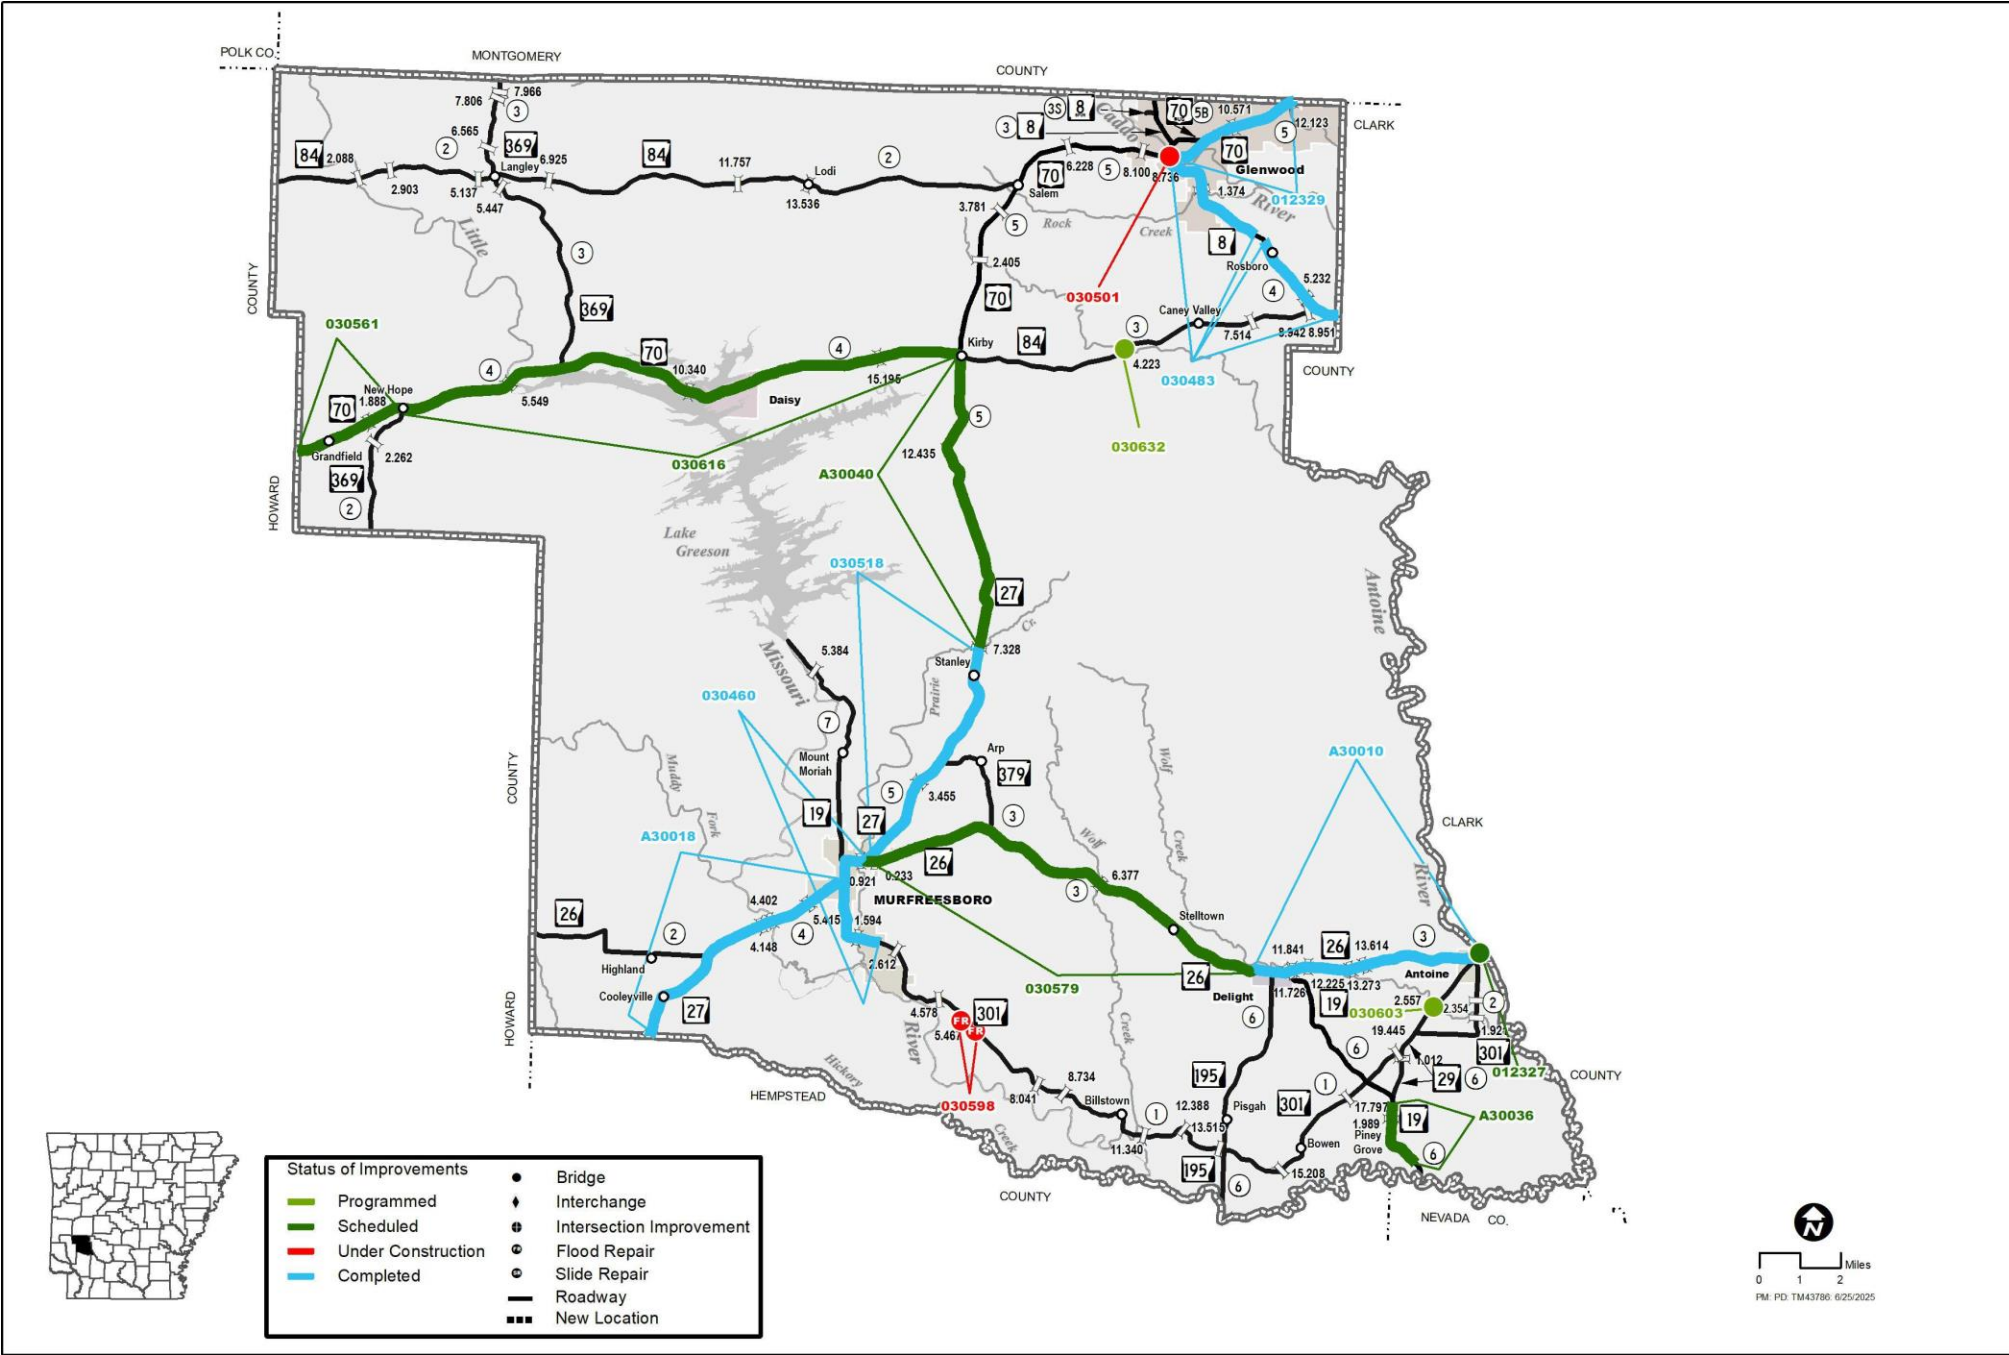

SUMMARY OF CONSTRUCTION PROJECTS
PIKE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012327	Antoine River Str. & Apprs. (S) Addt'l Rte.-Sec.: Clark 26-4	26	3	Structure & Approaches	Scheduled	2026		-	\$1 - \$3 M	-	\$3 - \$5 M
012329	Glenwood – Hwy. 227 (S) Addt'l Rte.-Sec.: Garland 70-8; Hot Spring 70-7; Montgomery 70-6	70	5	Resurfacing	Completed	May. 2019	Jun. 2020	3.07	\$1,034,001	18.14	\$6,032,225
012376*	Districts 3 & 7 Bridge Preservation (2021) (S) Addt'l Rte.-Sec.: Various	70	4	Bridge Rehabilitation	Sub. Completed	May. 2021	Jun. 2022	0.20	\$2,946,503	0.57	\$8,529,349
012392*	Hydrodemolition Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	26	3	Bridge Rehabilitation	Sub. Completed	Jun. 2022	Nov. 2023	-	\$877,356	-	\$5,942,622
012407*	Districts 2, 3 & 7 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various	26	3	Bridge Rehabilitation	Sub. Completed	Apr. 2022	Jun. 2024	-	\$16,266	-	\$5,195,000
012426*	Districts 3 & 7 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Completed	Apr. 2022	Jun. 2024	-	\$244,859	-	\$3,274,787
012445*	Districts 3, 4, 6, 7 & 8 Bridge Preservation (2023) (S) Addt'l Rte.-Sec.: Various	26	3	Bridge Rehabilitation	Completed	Mar. 2023	Apr. 2024	-	\$103,637	-	\$2,369,369
030405*	Glenwood Sidewalks (ATEP-11) (S)			Enhancement	Completed	Dec. 2012	Jun. 2016	-	\$291,225	-	\$291,225
030410*	Little Missouri River Trail (Ph. I) (Pike Co.) (S)			Enhancement	Completed	Nov. 2013	Apr. 2016	-	\$40,000	-	\$40,000
030448*	Glenwood Mt. View Rd. Sidewalks (ATEP-11) (S)			Enhancement	Completed	Apr. 2015	Nov. 2018	-	\$208,775	-	\$208,775
030460	Murfreesboro (Sel. Secs.) (Overlay) (S) Addt'l Rte.-Sec.: Pike 301-1	27	5	Resurfacing	Completed	May. 2016	Oct. 2016	3.30	\$929,619	3.30	\$929,619
030466*	City Park Walking Trail (Murfreesboro) (RTP-15) (S)			Enhancement	Completed	Oct. 2016	Jan. 2019	-	\$50,000	-	\$50,000
030473*	Hwy. 70B – Hwy. 70 Sidewalks (Glenwood) (TAP-15) (S)			Enhancement	Completed	May. 2018	Nov. 2021	-	\$483,500	-	\$483,500
030483	Hwy. 70 – Clark Co. Line (Sel. Secs.) (S)	8	4	Resurfacing	Completed	Apr. 2019	Oct. 2019	6.11	\$2,704,593	6.11	\$2,704,593
030495*	Murfreesboro City Park Trail Lighting (TAP-16) (S)			Enhancement	Completed	Feb. 2018	Mar. 2020	-	\$86,400	-	\$86,400
030499*	District 3 Sealing Program (2017) (S) Addt'l Rte.-Sec.: Various	27	5	Sealing	Completed		Mar. 2019	6.20	\$230,671	30.10	\$1,119,874
030501	Saline & Caddo Rivers Strs. & Apprs. (S) Addt'l Rte.-Sec.: Howard 278-2; Sevier 70-2	70	5	Structure & Approaches	Under Construction	Sep. 2020	Late 2025	0.52	\$6,070,855	1.76	\$20,547,510
030518	Murfreesboro – North (S)	27	5	Resurfacing	Completed	Apr. 2020	Nov. 2020	6.14	\$2,009,316	6.14	\$2,009,316
030541*	Glenwood Park St. and Hwy. 8 Sidewalks (TAP-18) (S)			Enhancement	Completed	Oct. 2022	Mar. 2024	-	\$781,341	-	\$781,341
030547*	District 3 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	26	2	Sealing	Completed		Jun. 2022	5.00	\$110,828	59.40	\$1,316,633

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

PIKE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
030561	Hwy. 278 – Hwy. 369 (S) Addt'l Rte.-Sec.: Howard 70-3	70	4	Resurfacing	Scheduled	2026		2.79	\$1 - \$3 M	8.80	\$3 - \$5 M
030579	Murfreesboro – Delight (S)	26	3	Resurfacing	Scheduled	2026		10.80	\$5 - \$10 M	10.80	\$5 - \$10 M
030589*	Glenwood Tennessee Ave. Sidewalks (TAP-20) (S)			Enhancement	Under Construction	Oct. 2022		-	\$241,734	-	\$241,734
030590*	Murfreesboro N. Washington St. Sidewalks (TAP-20) (S)			Enhancement	Completed	Dec. 2023	Jul. 2024	1.27	\$300,886	1.27	\$300,886
030598	Hwy. 301 Flood Damage Repairs (Pike Co.) (S)	301	1	Base Stabilization	Under Construction	Nov. 2024	Mid 2026	0.06	\$2,474,908	0.06	\$2,474,908
030603	Wolf Creek Str. & Apprs. (S)	29	6	Structure & Approaches	Programmed			0.21	\$3 - \$5 M	0.21	\$3 - \$5 M
030616	Hwy. 369 – Kirby (S)	70	4	Resurfacing	Scheduled	2026		14.43	\$3 - \$5 M	14.43	\$3 - \$5 M
030628*	Glenwood Mountain View Sidewalk Impvts. (TAP-23) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
030632	Antoine River Str. & Apprs. (S)	84	3	Structure & Approaches	Programmed			-	\$3 - \$5 M	-	\$3 - \$5 M
A30007*	District 3 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	84	3	Resurfacing	Completed		Jun. 2022	9.20	\$180,346	55.50	\$1,087,956
A30010	Delight – Clark Co. Line (S)	26	3	Resurfacing	Completed	Feb. 2022	Aug. 2022	5.72	\$4,019,436	5.72	\$4,019,436
A30016*	District 3 Resurfacing Program (2022) (S) Addt'l Rte.-Sec.: Various	195	6	Resurfacing	Completed	Jan. 2022	May. 2023	8.33	\$128,914	89.86	\$1,390,661
A30017*	District 3 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	84	3	Resurfacing	Completed	Jan. 2023	Aug. 2024	9.19	\$363,064	46.27	\$1,827,962
A30018	Howard Co. Line – Murfreesboro (S) Addt'l Rte.-Sec.: Hempstead 27-3	27	4	Resurfacing	Completed	May. 2023	Jun. 2024	6.30	\$3,341,237	10.45	\$5,542,211
A30026*	District 3 Resurfacing Program (2024) (S) Addt'l Rte.-Sec.: Various	195	6	Resurfacing	Programmed			8.33	< \$1 M	40.29	\$1 - \$3 M
A30036	Hwy. 29 – North (Sel. Secs.) (S) Addt'l Rte.-Sec.: Nevada 19-5	19	6	Resurfacing	Scheduled	2026		1.82	\$1 - \$3 M	4.03	\$1 - \$3 M
A30037*	District 3 Resurfacing Program (2025) (S) Addt'l Rte.-Sec.: Various	369	3	Resurfacing	Programmed			5.60	< \$1 M	40.10	\$1 - \$3 M
A30040	Prairie Creek – Hwy. 70 (S)	27	5	Resurfacing	Scheduled	2026		7.61	\$3 - \$5 M	7.61	\$3 - \$5 M
A30042*	District 3 Resurfacing Program (2026) (S) Addt'l Rte.-Sec.: Howard 278-2; Lafayette 53-4; Nevada 53-3, 387-1	84	2	Resurfacing	Programmed			13.35	-	35.83	-
C55001*	Glenwood Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	May. 2018	Sep. 2018	1.33	\$274,162	1.33	\$274,162
C55002*	Daisy Overlay & Surfactng (S)	CS		Resurfacing	Completed	Jan. 2021	Apr. 2021	1.17	\$494,453	1.17	\$494,453

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
PIKE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
C76031*	Antoine,mccaskill&murfrsboro Ovlay(slsecs)(s) Addt'l Rte.-Sec.: Hempstead CS	CS		Resurfacing	Completed	Feb. 2017	Jun. 2017	1.99	\$361,899	3.48	\$648,242
C76046*	Delight & Okolona Overlay (Sel. Secs.) (S) Addt'l Rte.-Sec.: Clark CS	CS		Resurfacing	Completed	May. 2018	Sep. 2018	1.23	\$197,828	3.14	\$505,026
C76060*	Antoine & Blevins Overlay (S) Addt'l Rte.-Sec.: Hempstead CS	CS		Resurfacing	Completed	Jan. 2023	Apr. 2023	0.42	\$81,894	1.81	\$382,425
C76064*	McCaskill & Murfreesboro Ovlay & Surfacing (S) Addt'l Rte.-Sec.: Hempstead CS	CS		Resurfacing	Sub. Completed	Jun. 2022	Oct. 2022	1.44	\$305,883	2.61	\$554,413
C76069*	Glenwood & Norman Overlay & Surf. (S) Addt'l Rte.-Sec.: Montgomery CS	CS		Resurfacing	Completed	Jan. 2023	May. 2023	1.39	\$400,137	2.77	\$724,504
SA5556*	Pike County Reseal No. 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2017	Oct. 2017	6.63	\$197,878	6.63	\$197,878
SA5557*	Pike County Surfacing No. 7 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Apr. 2018	Jun. 2018	6.84	\$436,420	6.84	\$436,420
SA5558*	Pike Co Pavement Markings No 3 (Sel Secs) (S)	CR		Safety Improvements	Completed	Sep. 2018	Nov. 2018	55.80	\$74,915	55.80	\$74,915
SA5559*	Pike County Reseal No. 5 (S)	CR		Resurfacing	Completed	Apr. 2020	Oct. 2020	13.79	\$705,995	13.79	\$705,995
SA5560*	Pike County Reseal No. 6 (S)	CR		Resurfacing	Completed	Jan. 2022	Jul. 2022	12.12	\$758,283	12.12	\$758,283
SA5561*	Pike Co. Surfacing No. 8 (S)	CR		Resurfacing	Under Construction	Jan. 2025	Late 2025	4.70	\$559,640	4.70	\$559,640
Totals For All Projects In Pike County								216.91	\$53,634,747		

* Job not shown on county map.
