


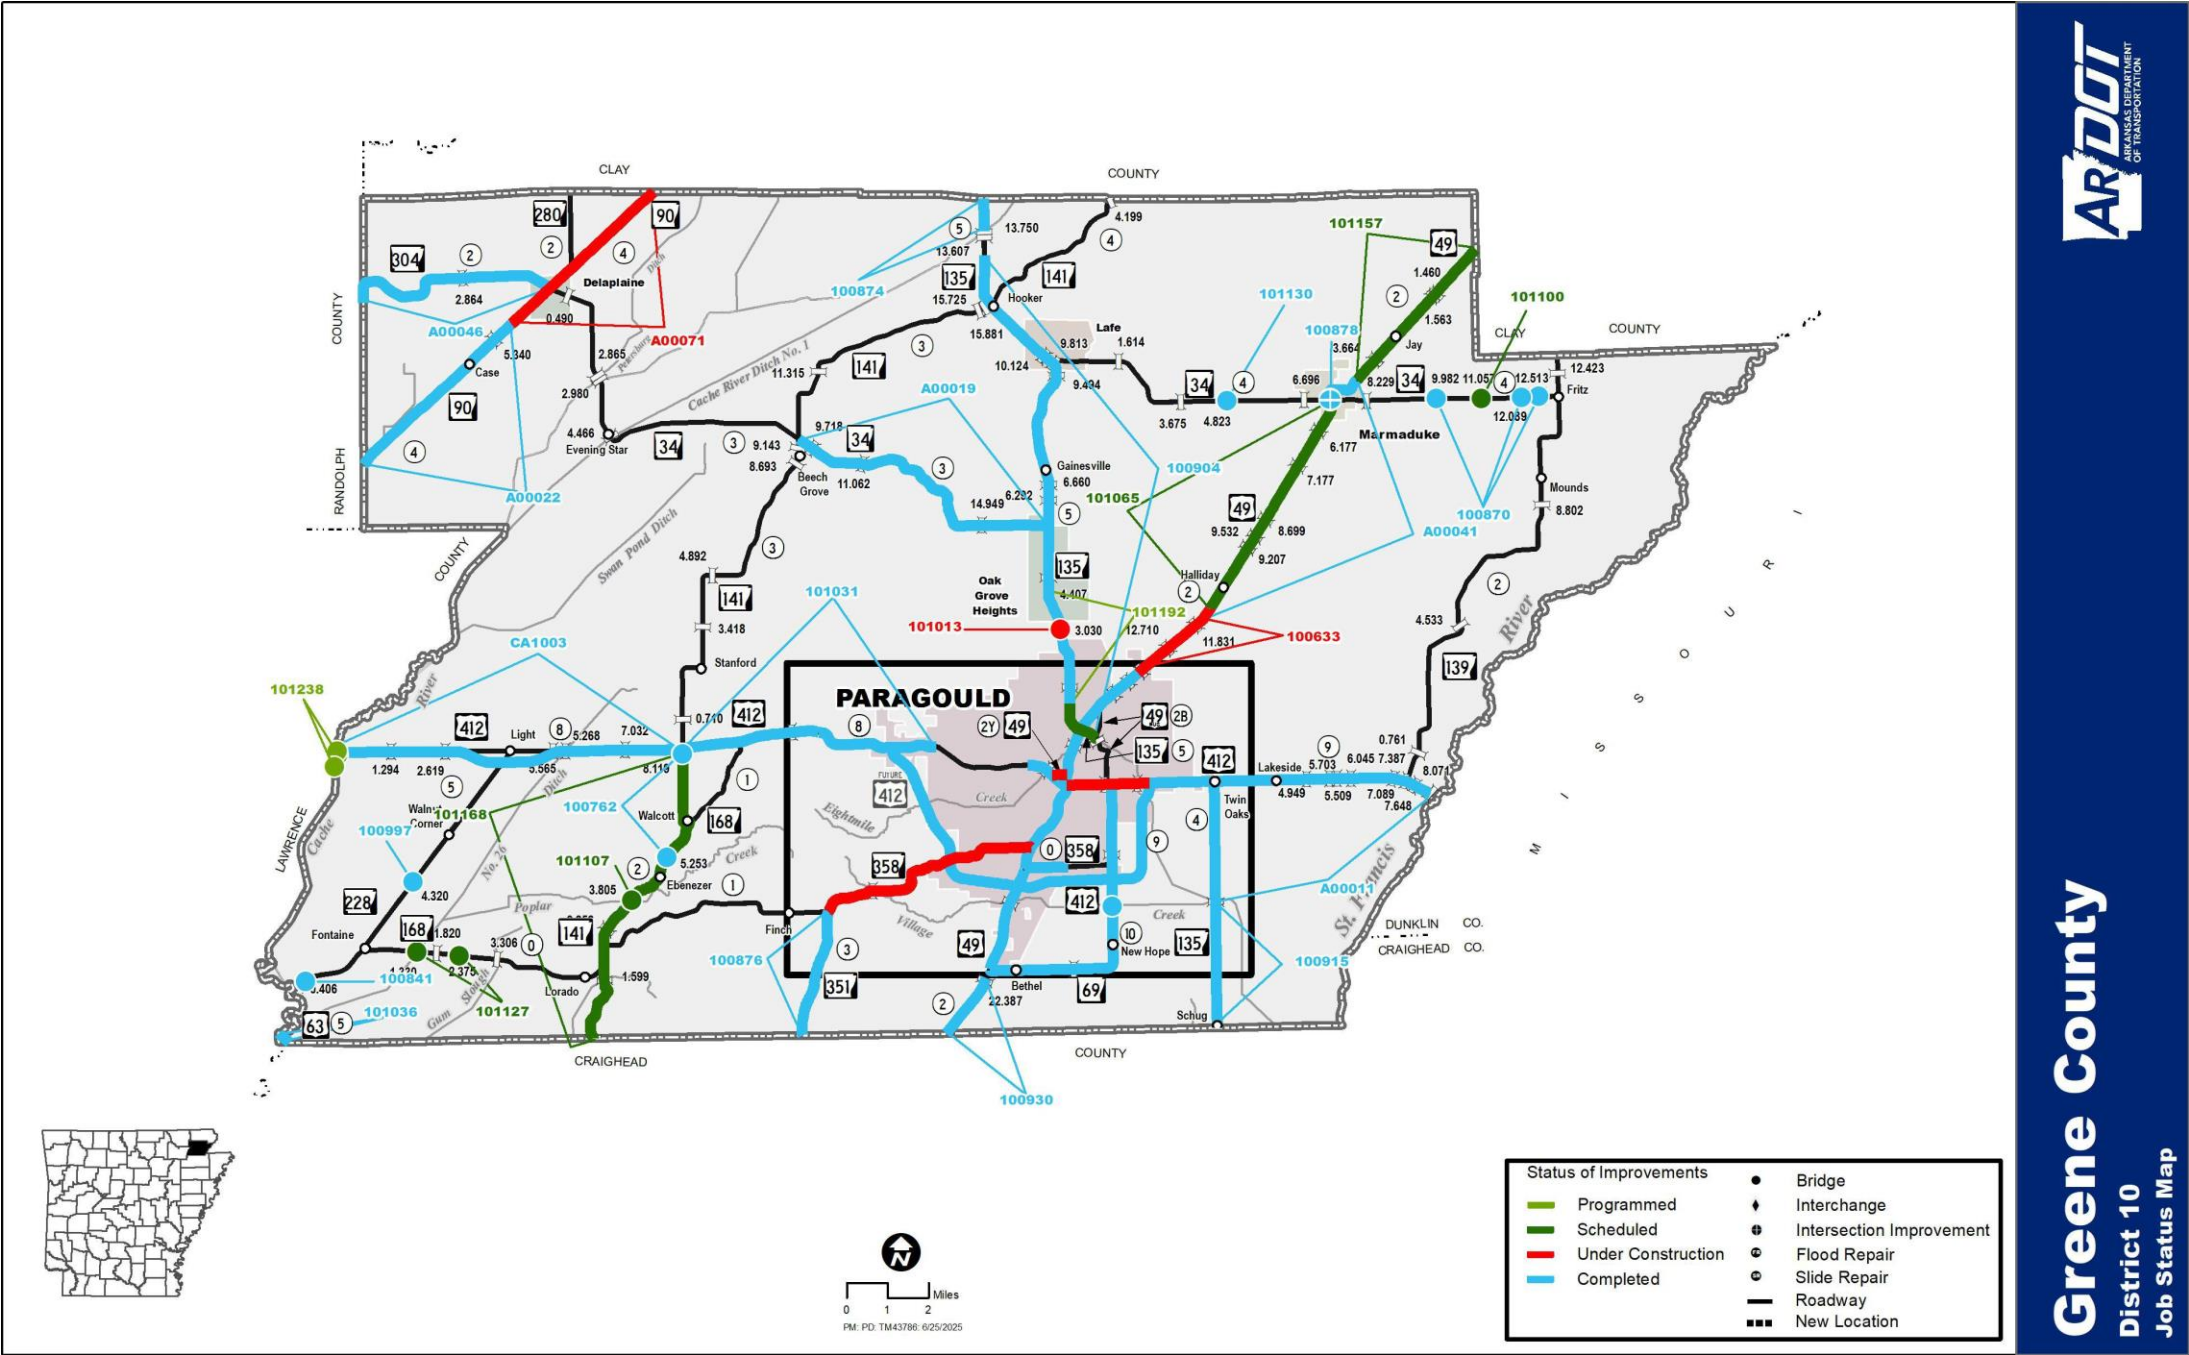

SUMMARY OF CONSTRUCTION PROJECTS

GREENE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
012378*	Districts 5 & 10 Bridge Preservation (2021) (S) Addt'l Rte.-Sec.: Various	90	4	Bridge Rehabilitation	Sub. Completed	May. 2021	Aug. 2022	0.04	\$925,012	0.38	\$8,787,616
012406*	Districts 1, 5, 6 & 10 Bridge Preservation (2022) (S) Addt'l Rte.-Sec.: Various			Bridge Rehabilitation	Sub. Completed	May. 2022	Oct. 2023	-	\$709,455	-	\$7,187,312
012424*	Districts 1, 5 & 10 Centerline Rumble Stripe Impvts. (S)			Safety Improvements	Completed	May. 2022	May. 2024	-	\$137,775	-	\$2,804,845
012444*	Districts 5, 9 & 10 Bridge Preservation (2023) (S) Addt'l Rte.-Sec.: Various	412	8B	Bridge Rehabilitation	Completed	Apr. 2023	Feb. 2024	0.87	\$1,298,587	2.37	\$3,537,528
012489	Hydrodemolition Bridge Preservation (2024) (S) Addt'l Rte.-Sec.: Various	412	9B	Bridge Rehabilitation	Scheduled	2026		-	< \$1 M	-	\$15 - \$20 M
012490	Districts 1, 5 & 10 Bridge Preservation (2024) (S) Addt'l Rte.-Sec.: Various	412	9B	Bridge Rehabilitation	Scheduled	2026		-	< \$1 M	-	\$1 - \$3 M
100278*	Hoxie – Jonesboro (PE) Addt'l Rte.-Sec.: Craighead 63-6; Lawrence 63-4	63	5	PE Only	Programmed			-	-	-	-
100632	Co. Rd. 845 – Hwy. 135 (Paragould) (S)	49	2	Major Widening	Completed	Sep. 2019	Jun. 2023	2.07	\$8,987,342	2.07	\$8,987,342
100633	Paragould – North (S)	49	2	Major Widening	Under Construction	Sep. 2024	<i>Mid 2027</i>	2.38	\$23,927,182	2.38	\$23,927,182
100708	Hwy. 412 West – Hwy. 49 (S)	New		New Location	Completed	Jan. 2017	Nov. 2020	5.18	\$12,768,505	5.18	\$12,768,505
100712	Hwy. 412 West – Hwy. 49 (Add'l. Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			5.23	\$10 - \$15 M	5.23	\$10 - \$15 M
100713	Hwy. 412 West – Hwy. 49 (Add'l. Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			5.23	\$10 - \$15 M	5.23	\$10 - \$15 M
100714	Hwy. 49 – Hwy. 412 East (Add'l. Lanes) (Gr. & Strs.) (F)	New		Grading & Structures	Programmed			5.20	\$20 - \$30 M	5.20	\$20 - \$30 M
100715	Hwy. 49 – Hwy. 412 East (Add'l. Lanes) (Bs. & Surf.) (F)	New		Base & Surfacing	Programmed			5.20	\$10 - \$15 M	5.20	\$10 - \$15 M
100762	Hwy. 358 – Hwy. 412 Strs. & Apprs. (S)	141	2	Structure & Approaches	Sub. Completed	Nov. 2021	Oct. 2023	0.14	\$1,609,500	0.14	\$1,609,500
100789*	Hwy. 69 R.R. Signal Upgrade (S. of Paragould) (S)	69	10	RR Crossing	Completed	May. 2013	Jun. 2017	-	\$138,078	-	\$138,078
100841	Cache River Relief Str. & Apprs. (S)	228	5	Structure & Approaches	Completed	Jun. 2019	Oct. 2020	0.20	\$1,449,706	0.20	\$1,449,706
100862*	Buttercup Ln. RR Signals (Paragould) (S)	CS		RR Crossing	Completed	Nov. 2021	Nov. 2021	-	\$295,892	-	\$295,892
100864*	CR 865 RR Signals (NE of Paragould) (S)	CR		RR Crossing	Completed	Oct. 2016	Jan. 2020	-	\$243,350	-	\$243,350
100870	Hwy. 34 Strs. & Apprs. (S)	34	4	Structure & Approaches	Completed	Sep. 2018	May. 2022	0.44	\$5,338,000	0.44	\$5,338,000
100874	Cache River – Hwy. 62 (S) Addt'l Rte.-Sec.: Clay 135-6	135	5	Resurfacing	Completed	Jan. 2020	Jun. 2020	0.80	\$235,320	10.84	\$3,188,595
100876	Craighead Co. Line – Hwy. 358 (S)	351	3	Resurfacing	Completed	May. 2018	Jul. 2019	3.14	\$804,729	3.14	\$804,729
100878	Hwy. 49/Hwy. 34 Inters. Impvts. (Marmaduke) (S) Addt'l Rte.-Sec.: Greene 49-2	34	4	Safety Improvements	Sub. Completed	Nov. 2020	May. 2023	0.13	\$1,714,999	0.13	\$1,714,999

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GREENE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
100893	Hwy. 49B – Hwy. 135 (Paragould) (S)	412	9	Resurfacing	Completed	Jan. 2017	Jul. 2017	2.67	\$1,282,756	2.67	\$1,282,756
100900	Hwys. 69 & 358 (Paragould) (Sel. Secs.) (S) Addt'l Rte.-Sec.: Greene 358-0	69	10	Resurfacing	Completed	May. 2017	Sep. 2017	8.36	\$2,662,592	8.36	\$2,662,592
100904	Hwy. 49B – Hooker (S)	135	5	Resurfacing	Completed	Apr. 2018	Aug. 2018	12.98	\$3,426,072	12.98	\$3,426,072
100915	Craighead Co. Line – North (S)	135	4	Resurfacing	Completed	Jan. 2018	Sep. 2018	3.10	\$837,459	3.10	\$837,459
100930	Hwy. 69 – South (Sel. Secs.) (S) Addt'l Rte.-Sec.: Craighead 49-3	49	2	Resurfacing	Completed	Feb. 2019	Sep. 2019	0.62	\$288,279	2.75	\$1,278,657
100951*	Paragould 8 Mile Creek Trail (TAP) (S)			Enhancement	Completed	Mar. 2021	Nov. 2022	-	\$1,195,000	-	\$1,195,000
100973*	District 10 Sealing Program (2018) (S) Addt'l Rte.-Sec.: Various	139	2	Sealing	Completed		Jul. 2020	7.78	\$107,393	80.48	\$1,110,923
100997	Buffalo Head Slough Str. & Apprs. (S)	228	5	Structure & Approaches	Sub. Completed	Apr. 2022	Sep. 2023	0.36	\$2,645,262	0.36	\$2,645,262
101000	Village Creek Str. & Apprs. (S)	69	10	Structure & Approaches	Sub. Completed	Sep. 2020	Dec. 2021	0.11	\$1,489,000	0.11	\$1,489,000
101013	Jacks Creek Str. & Apprs. (S)	135	5	Structure & Approaches	Under Construction	Nov. 2023	Late 2025	0.14	\$4,795,046	0.14	\$4,795,046
101031	Hwy. 141 – Paragould (S)	412	8	Resurfacing	Completed	May. 2020	Oct. 2020	6.39	\$1,372,705	6.39	\$1,372,705
101036	Lawrence Co. Line – S. of Bono (S) Addt'l Rte.-Sec.: Craighead 63-6	63	5	Resurfacing	Completed	May. 2020	Sep. 2020	0.27	\$73,876	7.27	\$1,989,184
101064*	District 10 Sealing Program (2020) (S) Addt'l Rte.-Sec.: Various	34	3	Sealing	Completed		Jun. 2022	6.30	\$120,629	67.84	\$1,298,960
101065	Marmaduke – S. of Halliday (S)	49	2	Major Widening	Scheduled	Sep. 2027		5.96	\$40 - \$50 M	5.96	\$40 - \$50 M
101096*	Paragould 8 Mile Creek Trail Ph. 4 (TAP-21) (S)			Enhancement	Under Construction	Oct. 2024		-	\$521,229	-	\$521,229
101100	Hwy. 34 Str. & Apprs. (Greene Co.) (S)	34	4	Structure & Approaches	Scheduled	Jan. 2026		0.54	\$3 - \$5 M	0.54	\$3 - \$5 M
101107	Poplar Creek Str. & Apprs. (S)	141	2	Structure & Approaches	Scheduled	2026		0.36	\$5 - \$10 M	0.36	\$5 - \$10 M
101127	Hwy. 168 Strs. & Apprs. (S)	168	0	Structure & Approaches	Scheduled	2026		0.55	\$3 - \$5 M	0.55	\$3 - \$5 M
101130	Hwy. 34 Str. & Apprs. (S)	34	4	Structure & Approaches	Sub. Completed	May. 2023	May. 2025	0.05	\$1,340,751	0.05	\$1,340,751
101133	Hwy. 49B – Fairview Rd. (Paragould) (S)	135	5	Major Widening	Scheduled	2026		1.22	\$5 - \$10 M	1.22	\$5 - \$10 M
101157	Piggott – Marmaduke (S) Addt'l Rte.-Sec.: Clay 49-1	49	2	Resurfacing	Scheduled	2026		4.33	\$1 - \$3 M	19.89	\$5 - \$10 M
101168	Co. Rd. 764 – Hwy. 412 (S) Addt'l Rte.-Sec.: Craighead 141-1	141	2	Resurfacing	Scheduled	2026		8.27	\$1 - \$3 M	12.42	\$3 - \$5 M
101179*	Studio Drift Crowley's Ridge Gravel Trail (Greene County) (RTP-23) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
101183*	Delaplaine Town Park Trail (TAP-23) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

GREENE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
101187*	District 10 Central Shop Impvts. (Paragould) (S)	New		Buildings	Programmed			-	< \$1 M	-	< \$1 M
101192	Fairview Rd. – Sunset Dr. (S)	135	5	Major Widening	Programmed			2.87	\$15 - \$20 M	2.87	\$15 - \$20 M
101238	Cache River Str. Removal & Scour Repair (S)	412	7	Bridge Rehabilitation Safety Improvements	Programmed			-	< \$1 M	-	< \$1 M
	Addt'l Rte.-Sec.: Lawrence 412-7										
A00005	Carroll Rd. – Hwy. 49 (Paragould) (S)	412	8B	Resurfacing	Completed	Feb. 2021	Jun. 2021	1.07	\$450,723	1.07	\$450,723
A00007*	District 10 Resurfacing Program (2021) (S)	141	4	Resurfacing	Completed		Jun. 2022	4.30	\$60,493	79.68	\$1,120,950
	Addt'l Rte.-Sec.: Various										
A00011	Eightmile Creek – Missouri State Line (S)	135	4	Resurfacing	Completed	Feb. 2022	Aug. 2022	8.07	\$4,324,853	8.07	\$4,324,853
	Addt'l Rte.-Sec.: Greene 412-9										
A00019	Hwy. 141 – Hwy. 135 (S)	34	3	Resurfacing	Completed	May. 2022	Oct. 2022	7.27	\$2,468,767	7.27	\$2,468,767
A00021	Hwy. 358 – Hwy. 69 (Paragould) (S)	49	2	Resurfacing	Completed	Feb. 2022	Oct. 2022	2.56	\$1,599,620	2.56	\$1,599,620
A00022	S. of Delaplaine – Randolph Co. Line (S)	90	4	Resurfacing	Sub. Completed	Apr. 2022	Aug. 2022	4.98	\$1,659,899	4.98	\$1,659,899
A00026*	District 10 Resurfacing Program (2022) (S)	228	5	Resurfacing	Completed	Jan. 2022	May. 2023	1.65	\$178,912	12.47	\$1,352,144
	Addt'l Rte.-Sec.: Various										
A00041	Marmaduke – Paragould (Sel. Secs.) (S)	49	2	Resurfacing	Sub. Completed	Mar. 2023	Oct. 2023	10.90	\$4,515,338	10.90	\$4,515,338
A00046	Randolph Co. Line – Delaplaine (S)	304	2	Resurfacing	Sub. Completed	Jun. 2023	Dec. 2023	5.48	\$2,197,385	5.48	\$2,197,385
A00051*	District 10 Resurfacing Program (2024) (S)	90	4	Resurfacing	Programmed			7.38	< \$1 M	42.11	\$1 - \$3 M
	Addt'l Rte.-Sec.: Various										
A00054*	Hwy. 49 – Hwy. 139 (S)	34	4	Resurfacing	Programmed			5.55	< \$1 M	5.55	< \$1 M
A00056*	Hwy. 141 Structures Repairs (Greene Co.) (S)	141	3	Structure & Approaches	Programmed			4.89	< \$1 M	4.89	< \$1 M
A00062	Hwy. 49 – Hwy. 412B (S)	412	9	Resurfacing	Completed	Jan. 2024	Jul. 2024	4.86	\$1,304,313	4.86	\$1,304,313
A00067*	District 10 Resurfacing Program (2025) (S)	168	0	Resurfacing	Programmed			1.00	< \$1 M	40.71	\$1 - \$3 M
	Addt'l Rte.-Sec.: Various										
A00071	Hwy. 412B – Peach Orchard (Sel. Secs.) (S)	90	4	Resurfacing	Under Construction	Nov. 2024	Late 2025	4.76	\$1,597,030	17.49	\$5,868,078
	Addt'l Rte.-Sec.: Clay 90-3; Lawrence 34-1, 67-17Y; Randolph 34-2, 90-5										
A00073	Hwys. 49Y, 358 & 412B Impvts. (Paragould) (S)	49	2Y	Resurfacing	Under Construction	Jan. 2025	Late 2025	8.09	\$3,093,681	8.09	\$3,093,681
	Addt'l Rte.-Sec.: Greene 358-1, 412-9B										
A00086*	District 10 Resurfacing Program (2026) (S)	34	4	Resurfacing	Programmed			10.37	-	39.44	-
	Addt'l Rte.-Sec.: Various										
C28001*	Oak Grove Heights Olay & Surf.(sel. Secs.)(s)	CS		Resurfacing	Completed	Jun. 2015	Sep. 2015	1.75	\$251,688	1.75	\$251,688

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS
GREENE COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
C28002*	Lafe & Marmaduke Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	May. 2016	Oct. 2016	3.78	\$489,340	3.78	\$489,340
C28003*	Oak Grove Heights Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	Jul. 2017	Oct. 2017	1.49	\$249,090	1.49	\$249,090
C28004*	Delaplaine Overlay (S)	CS		Resurfacing	Completed	Feb. 2020	Apr. 2020	1.18	\$154,137	1.18	\$154,137
C28005*	Paragould Overlay (S)	CS		Resurfacing	Completed	Feb. 2020	Sep. 2020	1.74	\$250,555	1.74	\$250,555
C28006*	Lafe Overlay & Surfacing (S)	CS		Resurfacing	Completed	Feb. 2021	May. 2021	1.56	\$246,999	1.56	\$246,999
C28007*	Oak Grove Heights Overlay No. 2 (S)	CS		Resurfacing	Completed	Feb. 2022	Sep. 2022	2.25	\$335,262	2.25	\$335,262
C28008*	Paragould Fairview & Shiloh Overlay (S)	CS		Resurfacing	Completed	Feb. 2024	Aug. 2024	4.23	\$883,997	4.23	\$883,997
C76051*	Marmaduke & Rector Overlay (S) Addt'l Rte.-Sec.: Clay CS	CS		Resurfacing	Completed	Jun. 2021	Nov. 2021	1.85	\$306,112	3.70	\$573,781
C76084*	Brookland Corning Marmaduke&rector Ovrly(s) Addt'l Rte.-Sec.: Clay CS; Craighead CS	CS		Resurfacing	Under Construction	Jan. 2025	Late 2025	1.65	\$262,352	7.32	\$1,163,889
CA1003	Hwy. 67 – Hwy. 141 (Widening) (S) Addt'l Rte.-Sec.: Lawrence 412-7	412	8	Major Widening	Sub. Completed	Jan. 2019	May. 2022	8.41	\$34,414,393	14.30	\$58,516,744
FA2808*	Hwy. 351 - West (Reconstruction) (S)	CR		Reconstruction	Completed	Sep. 2014	May. 2016	1.91	\$1,354,614	1.91	\$1,354,614
FA2809*	Hwy. 351 - West (Surfacing) (S)	CR		Resurfacing	Completed	May. 2016	Oct. 2016	1.91	\$300,305	1.91	\$300,305
SA2861*	Co. Road 32 Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2015	Sep. 2015	1.75	\$257,394	1.75	\$257,394
SA2862*	Greene Co. Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Aug. 2016	Nov. 2016	2.75	\$366,731	2.75	\$366,731
SA2864*	Green Co. Overlay No. 2 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Sep. 2018	Jun. 2019	3.89	\$578,603	3.89	\$578,603
SA2865*	Hwy. 135 - Cr 639 (Overlay & Surf.) (S)	CR		Resurfacing	Completed	May. 2021	Jul. 2021	2.04	\$323,172	2.04	\$323,172
SA2866*	Hwy. 412 - Hwy. 141 (Reseal) (S)	CR		Resurfacing	Completed	May. 2021	Sep. 2021	5.54	\$167,018	5.54	\$167,018
SA2867*	Paragould City Limits - Co. Rd. 274 (Overlay)	CR		Resurfacing	Sub. Completed	Jan. 2022	May. 2022	2.78	\$490,194	2.78	\$490,194
Totals For All Projects In Greene County								202.20	\$216,567,651		

* Job not shown on county map.
