


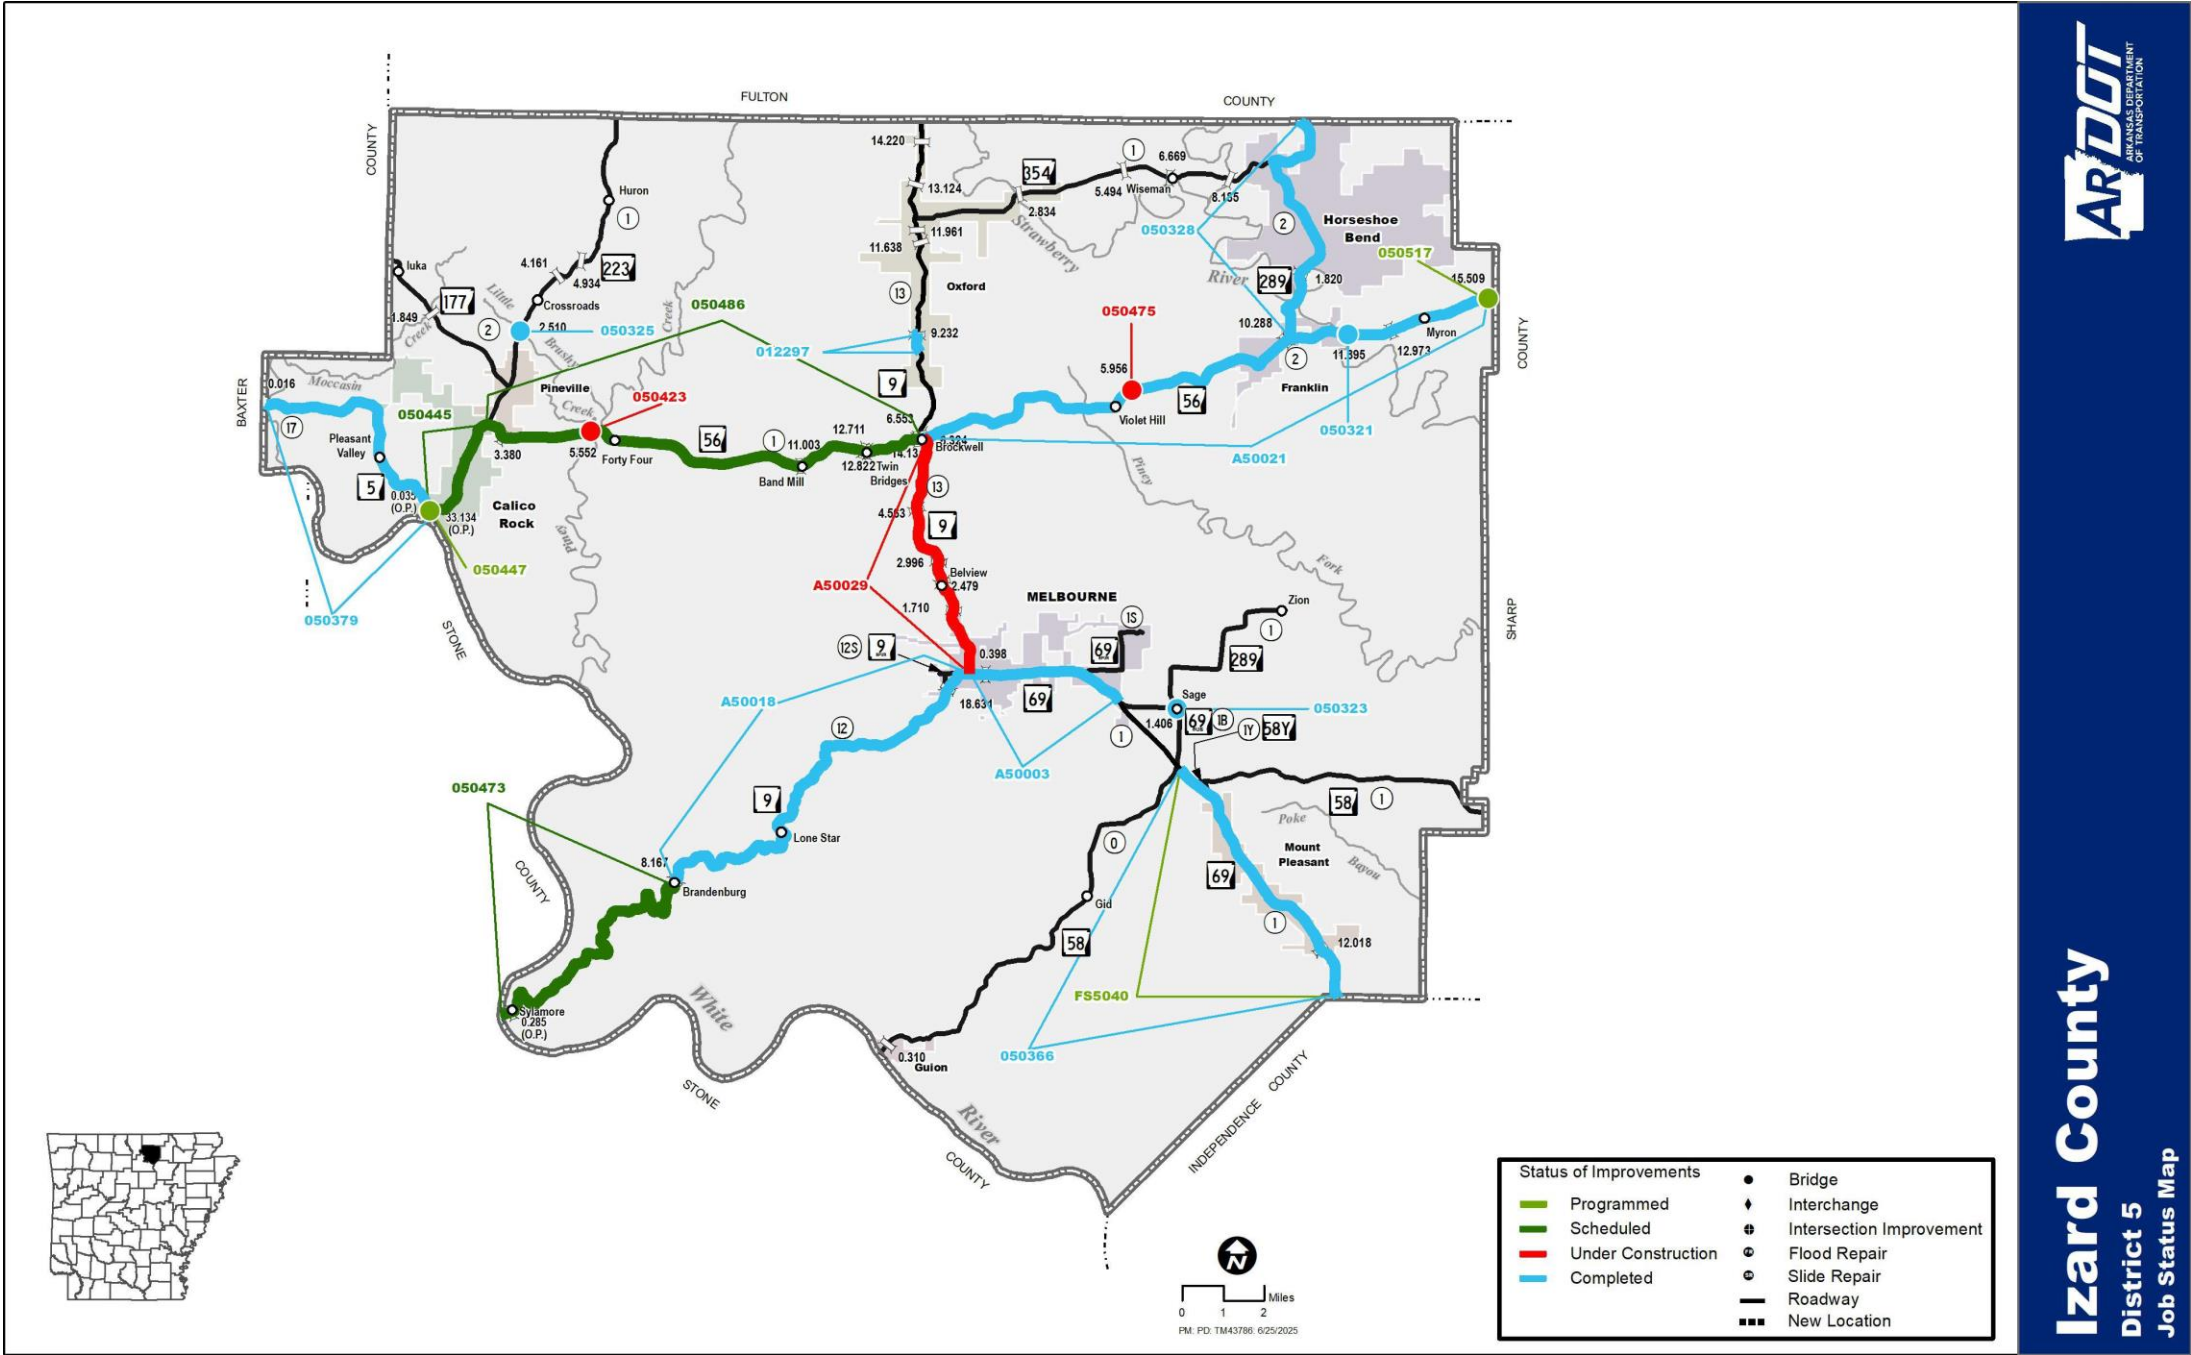

SUMMARY OF CONSTRUCTION PROJECTS  
IZARD COUNTY

| Job No. | Job Name                                                                                       | Rte. | Sec. | Type Work              | Status             | Let Date  | <i>Estimated or</i><br>Sub. Comp. | County Totals |             | Project Totals |             |
|---------|------------------------------------------------------------------------------------------------|------|------|------------------------|--------------------|-----------|-----------------------------------|---------------|-------------|----------------|-------------|
|         |                                                                                                |      |      |                        |                    |           | Date                              | Length (Mi)   | Cost        | Length (Mi)    | Cost        |
| 012297  | Districts 1, 5, 9 & 10 Pavement Friction Impvts. (Sel. Secs.) (S)<br>Addt'l Rte.-Sec.: Various | 9    | 13   | Safety Improvements    | Completed          | Apr. 2018 | Jul. 2019                         | 0.50          | \$239,250   | 4.66           | \$2,229,809 |
| 012351* | Districts 4, 5, 8 & 9 Bridge Preservation (2020) (S)<br>Addt'l Rte.-Sec.: Various              | 69   | 1    | Bridge Rehabilitation  | Completed          | May. 2020 | Aug. 2021                         | 0.03          | \$56,521    | 1.68           | \$3,165,189 |
| 012424* | Districts 1, 5 & 10 Centerline Rumble Stripe Impvts. (S)                                       |      |      | Safety Improvements    | Completed          | May. 2022 | May. 2024                         | -             | \$67,629    | -              | \$2,804,845 |
| 050025* | Park & Ride Lot Improvements (Dist. 5) (S)                                                     |      |      | Roadside Appurtenances | Programmed         |           |                                   | -             | < \$1 M     | -              | < \$1 M     |
| 050321  | Strawberry River Str. & Apprs. (S)                                                             | 56   | 2    | Structure & Approaches | Completed          | Sep. 2019 | Jul. 2022                         | 0.46          | \$3,393,000 | 0.46           | \$3,393,000 |
| 050323  | Ditch at L.M. 1.43 Str. & Apprs. (S)                                                           | 69   | 1B   | Structure & Approaches | Completed          | Sep. 2018 | May. 2019                         | 0.01          | \$584,374   | 0.01           | \$584,374   |
| 050325  | Little Brushy Creek Str. & Apprs. (S)                                                          | 223  | 1    | Structure & Approaches | Completed          | Oct. 2018 | Sep. 2021                         | 0.38          | \$1,910,640 | 0.38           | \$1,910,640 |
| 050328  | Hwy. 56 – Hwy. 62 (Overlay) (S)<br>Addt'l Rte.-Sec.: Fulton 289-3                              | 289  | 2    | Resurfacing            | Completed          | Mar. 2016 | Jul. 2016                         | 7.01          | \$880,598   | 10.09          | \$1,267,508 |
| 050331* | Wiseman Stream Mitigation Bank (S)                                                             |      |      | Miscellaneous          | Completed          |           | Dec. 2017                         | -             | \$363,910   | -              | \$363,910   |
| 050366  | Hwy. 69B – Independence Co. Line (S)                                                           | 69   | 1    | Resurfacing            | Completed          | May. 2017 | Oct. 2017                         | 7.17          | \$1,848,119 | 7.17           | \$1,848,119 |
| 050379  | Stone Co. Line – Baxter Co. Line (S)                                                           | 5    | 17   | Resurfacing            | Completed          | May. 2017 | May. 2018                         | 6.40          | \$2,562,004 | 6.40           | \$2,562,004 |
| 050383* | District 5 Sealing Program (2017) (S)<br>Addt'l Rte.-Sec.: Various                             | 56   | 2    | Sealing                | Completed          |           | Mar. 2019                         | 8.39          | \$175,873   | 51.16          | \$1,072,427 |
| 050423  | Piney Creek Str. & Apprs. (S)                                                                  | 56   | 1    | Structure & Approaches | Under Construction | Jan. 2024 | Mid 2027                          | 0.50          | \$6,520,000 | 0.50           | \$6,520,000 |
| 050434* | District 5 Sealing Program (2020) (S)<br>Addt'l Rte.-Sec.: Various                             | 58   | 1    | Sealing                | Completed          |           | Jun. 2022                         | 7.89          | \$124,201   | 86.76          | \$1,365,738 |
| 050445  | Hwy. 5 – Hwy. 223 (S)                                                                          | 56   | 1    | Resurfacing            | Scheduled          | 2026      |                                   | 2.84          | < \$1 M     | 2.84           | < \$1 M     |
| 050447  | Calico Creek Str. & Apprs. (Calico Rock) (S)                                                   | 56   | 1    | Structure & Approaches | Programmed         |           |                                   | 0.17          | \$3 - \$5 M | 0.17           | \$3 - \$5 M |
| 050473  | Stone Co. Line – Brandenburg (S)                                                               | 9    | 12   | Resurfacing            | Scheduled          | 2026      |                                   | 8.10          | \$3 - \$5 M | 8.10           | \$3 - \$5 M |
| 050475  | Little Piney Creek Str. & Apprs. (S)                                                           | 56   | 2    | Structure & Approaches | Under Construction | Jul. 2024 | Early 2026                        | 0.12          | \$2,012,449 | 0.12           | \$2,012,449 |
| 050486  | Hwy. 223 – Brockwell (S)                                                                       | 56   | 1    | Resurfacing            | Scheduled          | 2026      |                                   | 11.46         | \$1 - \$3 M | 11.46          | \$1 - \$3 M |
| 050500* | Hwy. 58 Crossing Impvts. (Guion) (S)                                                           | 58   | 0    | RR Crossing            | Programmed         |           |                                   | -             | < \$1 M     | -              | < \$1 M     |
| 050517  | Hars Creek Str. & Apprs. (S)                                                                   | 56   | 2    | Structure & Approaches | Programmed         |           |                                   | -             | \$1 - \$3 M | -              | \$1 - \$3 M |
| 050521* | Poke Bayou Str. & Apprs. (Izard Co.) (S)                                                       | CR   |      | Structure & Approaches | Programmed         |           |                                   | -             | < \$1 M     | -              | < \$1 M     |
| A50003  | Hwy. 9 – Hwy. 69B (Melbourne) (S)                                                              | 69   | 1    | Resurfacing            | Completed          | Apr. 2021 | Jul. 2021                         | 3.92          | \$716,017   | 3.92           | \$716,017   |
| A50006* | District 5 Resurfacing Program (2021) (S)<br>Addt'l Rte.-Sec.: Various                         | 58   | 0    | Resurfacing            | Completed          |           | Jun. 2022                         | 11.75         | \$184,240   | 85.68          | \$1,343,456 |
| A50018  | Brandenburg – Hwy. 69 (S)                                                                      | 9    | 12   | Resurfacing            | Completed          | Nov. 2023 | Jun. 2024                         | 11.24         | \$4,159,761 | 11.24          | \$4,159,761 |

\* Job not shown on county map.

# SUMMARY OF CONSTRUCTION PROJECTS

## IZARD COUNTY

| Job No. | Job Name                                                               | Rte. | Sec. | Type Work          | Status             | Let Date  | Estimated or Sub. Comp. Date | County Totals |             | Project Totals |             |
|---------|------------------------------------------------------------------------|------|------|--------------------|--------------------|-----------|------------------------------|---------------|-------------|----------------|-------------|
|         |                                                                        |      |      |                    |                    |           |                              | Length (Mi)   | Cost        | Length (Mi)    | Cost        |
| A50021  | Hwy. 9 – Hwy. 167 (S)<br>Addt'l Rte.-Sec.: Sharp 56-3                  | 56   | 2    | Resurfacing        | Sub. Completed     | Apr. 2023 | Sep. 2023                    | 15.21         | \$3,971,512 | 19.70          | \$5,143,905 |
| A50024* | District 5 Resurfacing Program (2024) (S)<br>Addt'l Rte.-Sec.: Various | 58   | 0    | Resurfacing        | Programmed         |           |                              | 13.47         | < \$1 M     | 70.40          | \$1 - \$3 M |
| A50029  | Hwy. 69 – Hwy. 56 (S)                                                  | 9    | 13   | Resurfacing        | Under Construction | Nov. 2024 | Late 2025                    | 6.38          | \$2,259,294 | 6.38           | \$2,259,294 |
| A50034* | District 5 Resurfacing Program (2025) (S)<br>Addt'l Rte.-Sec.: Various | 58   | 1    | Resurfacing        | Programmed         |           |                              | 7.88          | < \$1 M     | 76.99          | \$1 - \$3 M |
| A50035  | Hwy. 9 Slide Repairs (Izard Co.) (S)                                   | 9    | 12   | Base Stabilization | Programmed         |           |                              | -             | < \$1 M     | -              | < \$1 M     |
| A50039* | District 5 Resurfacing Program (2026) (S)<br>Addt'l Rte.-Sec.: Various | 58   | 0    | Resurfacing        | Programmed         |           |                              | 19.64         | -           | 67.43          | -           |
| C33003* | Oxford Overlay (Sel. Sec.) (S)                                         | CS   |      | Resurfacing        | Completed          | May. 2016 | Oct. 2016                    | 2.06          | \$218,803   | 2.06           | \$218,803   |
| C33004* | Franklin Melbourne Mt Pleasant Overlay (Sel S                          | CS   |      | Resurfacing        | Completed          | Jun. 2018 | Dec. 2018                    | 6.01          | \$607,919   | 6.01           | \$607,919   |
| C33005* | Horseshoe Bend E. Tri-Lakes Dr. Overlay (S)                            | CS   |      | Resurfacing        | Completed          | Apr. 2019 | Jun. 2019                    | 1.62          | \$251,627   | 1.62           | \$251,627   |
| C33006* | Calico Rock Overlay (Sel. Secs.) (S)                                   | CS   |      | Resurfacing        | Completed          | May. 2019 | Oct. 2019                    | 1.24          | \$358,159   | 1.24           | \$358,159   |
| C33007* | Pineville Overlay (S)                                                  | CS   |      | Resurfacing        | Completed          | Apr. 2021 | Oct. 2021                    | 1.98          | \$232,886   | 1.98           | \$232,886   |
| C33008* | Calico Rock, Melbourne & Oxford Overlay & Sur                          | CS   |      | Resurfacing        | Completed          | Apr. 2023 | Aug. 2023                    | 3.53          | \$913,993   | 3.53           | \$913,993   |
| C33009* | Mount Pleasant Overlay & Surfacing (S)                                 | CS   |      | Resurfacing        | Completed          | Mar. 2023 | Jun. 2023                    | 1.72          | \$336,147   | 1.72           | \$336,147   |
| C33010* | Horseshoe Bend E. Tri-Lakes Drive Overlay No.                          | CS   |      | Resurfacing        | Completed          | Apr. 2023 | Oct. 2023                    | 1.36          | \$326,185   | 1.36           | \$326,185   |
| FS5040  | Independence Co. Line – North (S)                                      | 69   | 1    | Resurfacing        | Programmed         |           |                              | 7.17          | \$1 - \$3 M | 7.17           | \$1 - \$3 M |
| SA3342* | Hwy. 58-East (Overlay) (Sel. Secs.) (S)                                | CR   |      | Resurfacing        | Completed          | Jun. 2015 | Aug. 2015                    | 1.00          | \$133,405   | 1.00           | \$133,405   |
| SA3343* | Co. Rd 36 (Base&surfacing) (Sel. Secs.) (S)                            | CR   |      | Resurfacing        | Completed          | Jun. 2015 | Oct. 2015                    | 1.18          | \$221,779   | 1.18           | \$221,779   |
| SA3344* | Izard Co. Surfacing No. 15 (Sel. Secs.) (S)                            | CR   |      | Resurfacing        | Completed          | Aug. 2016 | Nov. 2016                    | 3.72          | \$629,432   | 3.72           | \$629,432   |
| SA3345* | Izard Co. Overlay No. 10 (Sel. Secs.) (S)                              | CR   |      | Resurfacing        | Completed          | Feb. 2018 | Nov. 2018                    | 3.25          | \$422,623   | 3.25           | \$422,623   |
| SA3346* | County Road 3 Surfacing (S)                                            | CR   |      | Resurfacing        | Completed          | May. 2019 | Jul. 2019                    | 1.00          | \$119,498   | 1.00           | \$119,498   |
| SA3347* | County Roads 9 & 112 Reseal (S)                                        | CR   |      | Resurfacing        | Completed          | May. 2019 | Aug. 2019                    | 5.68          | \$246,496   | 5.68           | \$246,496   |
| SA3348* | Izard Co. Reseal (S)                                                   | CR   |      | Sealing            | Completed          | Feb. 2021 | Oct. 2021                    | 8.28          | \$473,230   | 8.28           | \$473,230   |
| SA3349* | Izard Co. Level & Reseal (S)                                           | CR   |      | Resurfacing        | Sub. Completed     | Jan. 2022 | Aug. 2022                    | 4.08          | \$316,872   | 4.08           | \$316,872   |
| SA3350* | Co. Rd. 3 Overlay (S)                                                  | CS   |      | Resurfacing        | Completed          | Jan. 2024 | Apr. 2024                    | 1.05          | \$284,737   | 1.05           | \$284,737   |
| SA3351* | Izard Co. Level & Reseal No. 2 (S)                                     | CS   |      | Resurfacing        | Completed          | Jan. 2024 | Jun. 2024                    | 3.18          | \$296,745   | 3.18           | \$296,745   |
| SA3352* | Hwy. 69S – Co. Rd. 57 (Overlay) (S)                                    | CR   |      | Resurfacing        | Under Construction | Apr. 2025 | Late 2025                    | 1.20          | \$191,304   | 1.20           | \$191,304   |
| SA3353* | Co. Rd. 6 Reseal (S)                                                   | CR   |      | Resurfacing        | Under Construction | Apr. 2025 | Late 2025                    | 2.00          | \$86,189    | 2.00           | \$86,189    |

\* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

IZARD COUNTY

| IZARD COUNTY                             |          |      |      |           |        |          | <i>Estimated or</i><br>Sub. Comp. | County Totals |              | Project Totals |      |
|------------------------------------------|----------|------|------|-----------|--------|----------|-----------------------------------|---------------|--------------|----------------|------|
| Job No.                                  | Job Name | Rte. | Sec. | Type Work | Status | Let Date | Date                              | Length (Mi)   | Cost         | Length (Mi)    | Cost |
| Totals For All Projects In Iazard County |          |      |      |           |        |          |                                   | 164.90        | \$45,497,421 |                |      |

\* Job not shown on county map.
