


Status of Improvements	
— Programmed	● Bridge
— Scheduled	◆ Interchange
— Under Construction	⊕ Intersection Improvement
— Completed	⊙ Flood Repair
	⊙ Slide Repair
	— Roadway
	⋯ New Location

Woodruff County

District 1
Job Status Map

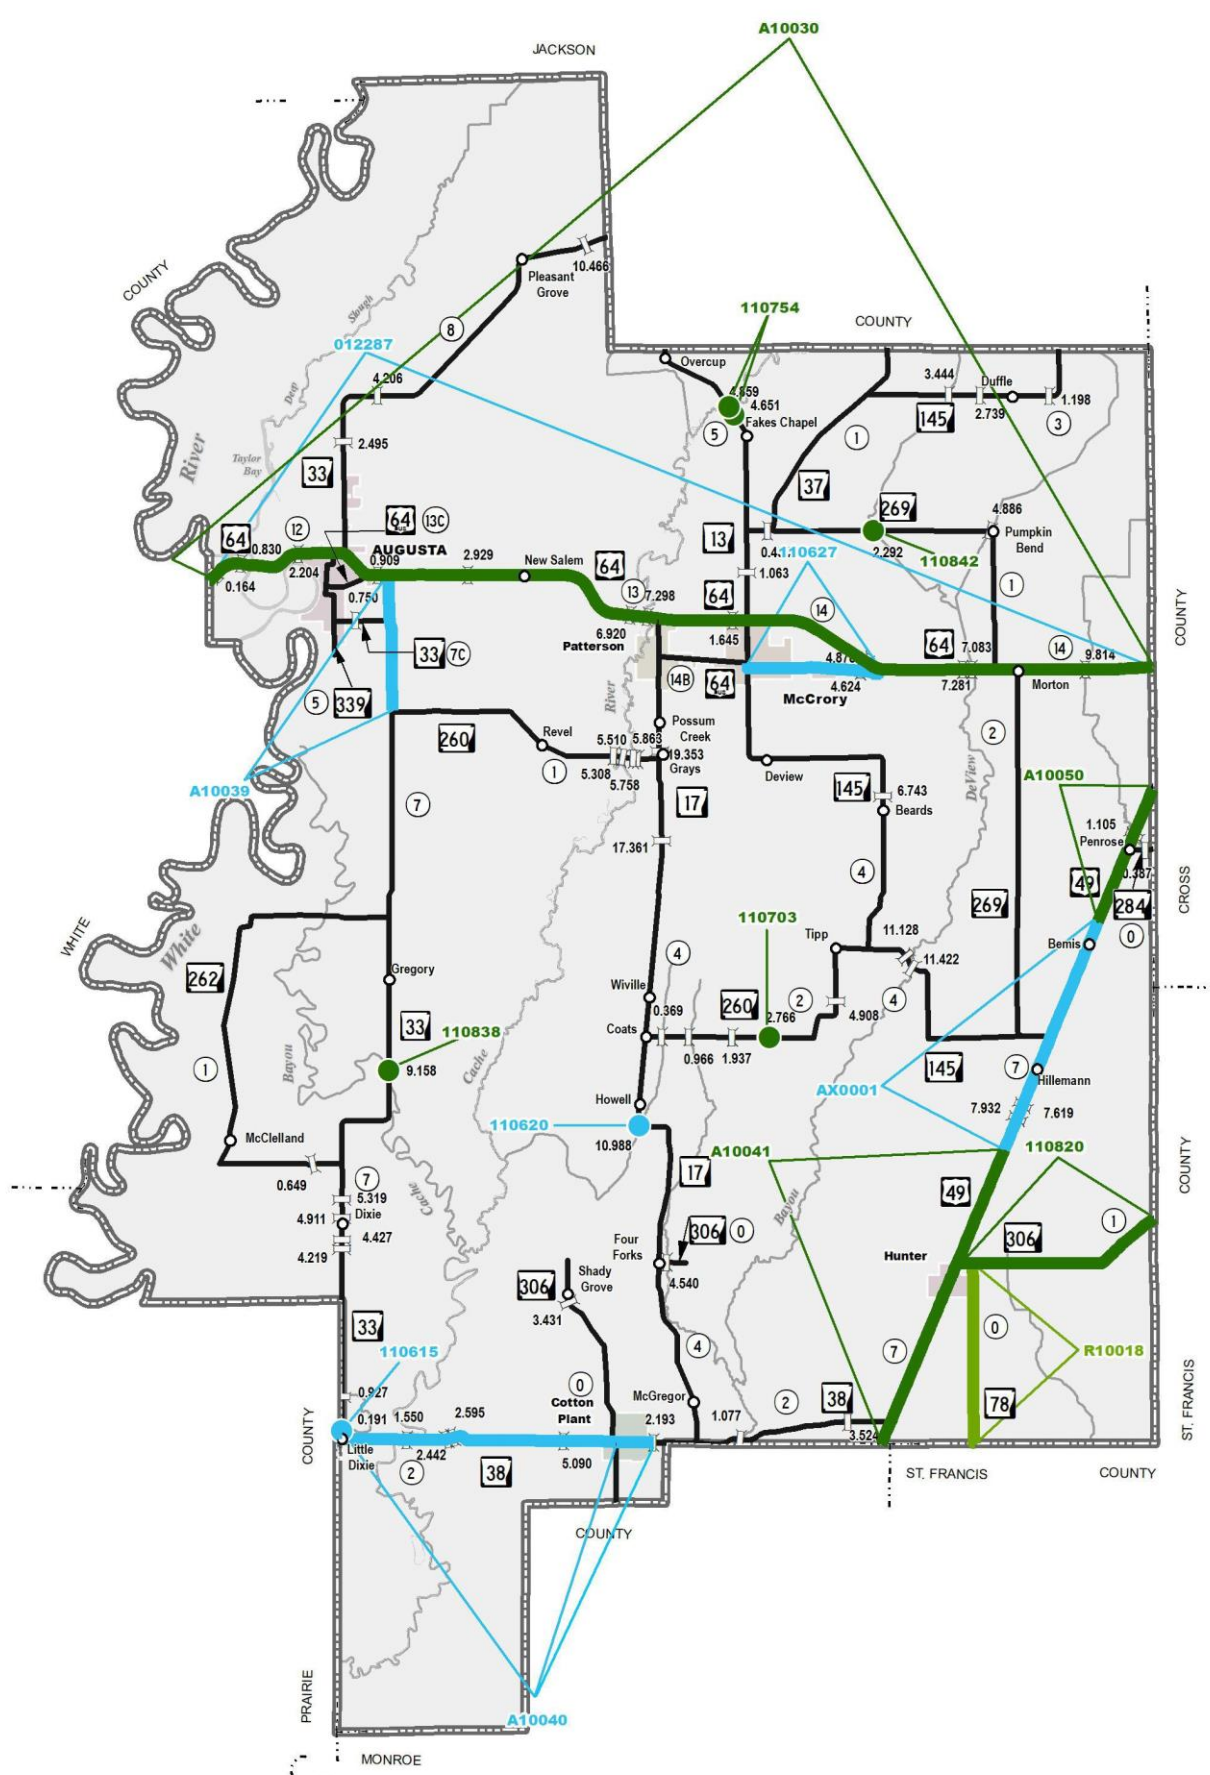

SUMMARY OF CONSTRUCTION PROJECTS

WOODRUFF COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
							Date	Length (Mi)	Cost	Length (Mi)	Cost
012287	Hwy. 367 – Crittenden Co. Line (S) Addt'l Rte.-Sec.: Cross 64-15/16; White 64-11; Woodruff 64-13/14	64	12	Resurfacing	Completed	Jul. 2017	Dec. 2018	22.09	\$6,675,593	62.51	\$18,890,509
012442*	Hydrodemolition Bridge Preservation (2023) (S) Addt'l Rte.-Sec.: Various	64	14	Bridge Rehabilitation	Under Construction	Mar. 2023	Oct. 2025	0.12	\$1,296,760	1.23	\$13,291,784
012443*	Districts 1 & 2 Bridge Preservation (2023) (S) Addt'l Rte.-Sec.: Various	38	2	Bridge Rehabilitation	Completed	Apr. 2023	May. 2024	0.07	\$112,060	5.00	\$8,004,308
110615	Hwy. 33 Str. & Apprs. (S)	33	7	Structure & Approaches	Completed	Oct. 2018	Nov. 2019	0.02	\$798,527	0.02	\$798,527
110620	Ditch at L.M. 10.96 Str. & Apprs. (S)	17	4	Structure & Approaches	Completed	Jan. 2019	Oct. 2019	0.04	\$825,973	0.04	\$825,973
110627	Hwy. 145 – Hwy. 64 (Overlay) (S)	64	14B	Resurfacing	Completed	Mar. 2016	Sep. 2016	3.15	\$343,869	3.15	\$343,869
110678*	District 1 Sealing Program (2017) (S) Addt'l Rte.-Sec.: Various	78	0	Bridge Rehabilitation Sealing	Completed		Mar. 2019	10.72	\$159,826	71.84	\$1,071,068
110685*	District 1 Sealing Program (2018) (S) Addt'l Rte.-Sec.: Various	145	4	Sealing	Completed		Dec. 2019	14.24	\$204,557	89.38	\$1,284,899
110703	Locust Slough Str. & Apprs. (S)	260	2	Structure & Approaches	Scheduled	2029		0.17	< \$1 M	0.17	< \$1 M
110723*	McCrary Hwy. 145 Sidewalks (TAP-18) (S)			Enhancement	Completed	Apr. 2020	Sep. 2020	0.28	\$111,250	0.28	\$111,250
110726*	Hwy. 17 RR Signals Upgrade (Patterson) (S)	17	4	RR Crossing	Completed	Oct. 2019	Nov. 2022	-	\$321,273	-	\$321,273
110754	Cache River & Relief Strs. & Apprs. (S)	17	5	Structure & Approaches	Scheduled	Aug. 2026		0.80	\$20 - \$30 M	0.80	\$20 - \$30 M
110764*	Augusta School District Sidewalks & Trail (TAP-21) (S)			Enhancement	Under Construction	May. 2024		-	\$142,325	-	\$142,325
110820	Hwy. 49 – Hwy. 193 (S) Addt'l Rte.-Sec.: St. Francis 306-2	306	1	Resurfacing	Scheduled	2027		4.76	\$1 - \$3 M	15.12	\$5 - \$10 M
110838	Cache Bayou Str. & Apprs. (S)	33	7	Structure & Approaches	Scheduled	2030		-	\$1 - \$3 M	-	\$1 - \$3 M
110842	Hwy. 269 Str. & Apprs. (Woodruff Co.) (S)	269	1	Structure & Approaches	Scheduled	2030		-	\$3 - \$5 M	-	\$3 - \$5 M
110866*	Augusta School District Walking and Biking Trail Ph. 2 (TAP-24) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
110869*	Woodruff Co. Cache River Water Trail (RTP-24) (S)			Enhancement	Programmed			-	< \$1 M	-	< \$1 M
A10009*	District 1 Resurfacing Program (2021) (S) Addt'l Rte.-Sec.: Various	33	7	Resurfacing	Completed		Jun. 2022	22.67	\$361,001	85.83	\$1,366,771
A10017*	District 1 Resurfacing Program (2023) (S) Addt'l Rte.-Sec.: Various	17	5	Resurfacing	Completed	Jan. 2023	Feb. 2024	17.88	\$599,775	60.99	\$2,045,880
A10018*	Hwy. 38 Str. & Apprs. (Woodruff Co.) (S)	38	2	Structure & Approaches	Completed	Sep. 2022	Nov. 2022	-	\$795,000	-	\$795,000

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

WOODRUFF COUNTY

Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Estimated or Sub. Comp. Date	County Totals		Project Totals	
								Length (Mi)	Cost	Length (Mi)	Cost
A10026*	District 1 Resurfacing Program (2024) (S) Addt'l Rte.-Sec.: Various	17	5	Resurfacing	Programmed			18.28	< \$1 M	36.42	\$1 - \$3 M
A10030	White Co. Line – Crittenden Co. Line (Sel. Secs.) (S) Addt'l Rte.-Sec.: Cross 64-15/16; Woodruff 64-13/14	64	12	Resurfacing	Scheduled	2027		22.10	\$1 - \$3 M	53.45	\$1 - \$3 M
A10039	Hwy. 260 – Hwy. 64 (S)	33	7	Resurfacing	Completed	Feb. 2024	Sep. 2024	3.03	\$893,973	3.03	\$893,973
A10040	Prairie Co. Line – Hwy. 17 (S)	38	2	Resurfacing	Completed	Jan. 2025	Jun. 2025	7.08	\$1,460,093	7.08	\$1,460,093
A10041	North of Hunter – Monroe Co. Line (S)	49	7	Resurfacing	Scheduled	Nov. 2025		7.13	\$1 - \$3 M	7.13	\$1 - \$3 M
A10042*	District 1 Resurfacing Program (2025) (S) Addt'l Rte.-Sec.: Various	269	1	Resurfacing	Programmed			2.00	< \$1 M	33.62	\$1 - \$3 M
A10048*	District 1 Resurfacing Program (2026) (S) Addt'l Rte.-Sec.: Various	260	2	Resurfacing	Programmed			6.79	< \$1 M	31.20	\$1 - \$3 M
A10050	Hickory Ridge – Hwy. 17 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Cross 49-6; Woodruff 49-8	49	7	Resurfacing	Scheduled	Nov. 2025		8.88	\$1 - \$3 M	18.64	\$5 - \$10 M
AX0001	Hwys. 29, 49 & 167 (Sel. Secs.) (S) Addt'l Rte.-Sec.: Cleveland 167-8; Hempstead 29-4	49	7	Resurfacing	Completed	Jan. 2021	Jul. 2021	5.50	\$528,045	15.94	\$1,530,369
C74003*	Patterson Overlay (Sel. Secs.) (S)	CS		Resurfacing	Completed	May. 2017	Oct. 2017	2.11	\$193,213	2.11	\$193,213
C74004*	Ctt'n Plnt& McCrory Ovrl'y & Surf (Sel Secs)(s)	CS		Resurfacing	Completed	Apr. 2018	Jun. 2018	3.64	\$484,730	3.64	\$484,730
C74006*	Augusta Overlay No. 2 (S)	CS		Resurfacing	Completed	Jan. 2021	Oct. 2021	2.13	\$229,376	2.13	\$229,376
C74007*	Hunter Overlay & Surfacing (S)	CS		Resurfacing	Completed	Feb. 2021	Jul. 2021	1.97	\$231,451	1.97	\$231,451
C76028*	Augusta & Tupelo Overlay (Sel. Secs.) (S) Addt'l Rte.-Sec.: Jackson CS	CS		Resurfacing	Completed	Feb. 2016	May. 2016	1.86	\$208,012	3.91	\$437,272
C76073*	Beedeville & McCrory Overlay & Surfacing (S) Addt'l Rte.-Sec.: Jackson CS	CS		Resurfacing	Completed	Apr. 2023	Dec. 2023	1.22	\$282,000	1.77	\$465,094
SA7442*	Woodruff Co. Surfacing No. 3 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jul. 2015	Oct. 2015	0.25	\$191,439	0.25	\$191,439
SA7443*	Woodruff Co. Reseal No. 10 (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2016	Aug. 2016	4.00	\$111,536	4.00	\$111,536
SA7444*	Woodruff Co. Overlay (Sel. Secs.) (S)	CR		Resurfacing	Completed	Jun. 2016	Aug. 2016	1.94	\$227,213	1.94	\$227,213
SA7445*	Woodruff Co. Surfacing No. 4 (Sel. Secs.) (S)	CR		Resurfacing	Completed	May. 2018	Oct. 2018	3.35	\$368,514	3.35	\$368,514
SA7446*	Woodruff Co. Overlay No. 2 (S)	CR		Resurfacing	Completed	Feb. 2020	May. 2020	3.61	\$472,578	3.61	\$472,578
SA7447*	Co. Rd. 25 - West (Overlay) (S)	CR		Resurfacing	Sub. Completed	Apr. 2022	Oct. 2022	2.63	\$460,085	2.63	\$460,085
SA7448*	Hwy. 33 – Hwy. 260 (Level & Reseal) (S)	CR		Resurfacing	Sub. Completed	Apr. 2024	Jul. 2024	8.30	\$364,051	8.30	\$364,051
SA7449*	Hwy. 145 – South (Level & Seal) (S)	CR		Resurfacing	Under Construction	May. 2025	Oct. 2025	3.77	\$357,852	3.77	\$357,852

* Job not shown on county map.

SUMMARY OF CONSTRUCTION PROJECTS

WOODRUFF COUNTY

WOODRUFF COUNTY							<i>Estimated or</i> Sub. Comp.	County Totals		Project Totals	
Job No.	Job Name	Rte.	Sec.	Type Work	Status	Let Date	Date	Length (Mi)	Cost	Length (Mi)	Cost
Totals For All Projects In Woodruff County								191.51	\$58,190,950		

* Job not shown on county map.
